



SHRIKHANDE CONSULTANTS LIMITED

MONTHLY PROGRESS REPORT

SATIS THANE

FOR JULY 2026

PROJECT MANAGEMENT CONSULTANTS

Reporting Period	01/07/2026 – 31/07/2026
MPR Version	v1

Office No. 2012 – 2013, 2nd Floor,
Akshar Business Park Wing – D,
Plot No. 3, Sector – 25, Near APMC,
Vashi, Navi Mumbai – 400 703
Tel. No.: (022) 2784 4440 / 3305 / 4199
E-mail: scplvashi@gmail.com
Web: www.scplasia.com

I N D E X

Sr. No.	SUBJECT
1	Executive Summary
2	Salient Features of the Project
3	Contractual Obligations
4	Progress
4.1	Physical Progress
4.2	Bar Chart (Planned vs. Actual)
4.3	Financial Progress & Gross Monthly Work Done Value
4.4	Important Events
5	Quality Performance
5.1	Material Testing / Frequency Chart
6	Bottlenecks
7	Next Month Program
8	List of Plant and Machinery
9	Laboratory Equipment at Site
10	Status of Drawings
10.1	Drawings Received
10.2	Drawings Balance
11	Material Received at Site
12	Safety Aspect
13	Meetings / Site Visits
14	Manpower Deployed (PMC)
15	Labour Man-Day Bar Chart
16	Photographs

1. EXECUTIVE SUMMARY

PHYSICAL PROGRESS BILLED TILL DATE

Target	Not Available
Actual	20.90%

Reporting-month planned physical progress is not available for 2026-07.

FINANCIAL PROGRESS BILLED TILL DATE

Target	Rs. 54,925,279.00
Actual	Rs. 55,376,980.00

STATUS SUMMARY

Physical Progress: Cumulative physical progress 20.9%; reporting-month planned target for 2026-07 is not available.

Financial Billed: Cumulative billed Rs. 55,376,980.00 against contract target Rs. 54,925,279.00.

Time Status: Project status: At Risk; time progress 99%.

EOT: Latest approved EOT-13 (1362 days); revised completion 2026-08-31.

Financial: Cost status: No Data; CPI Not Available.

Quality: Pass 99.99% (7560/7561 conducted).

Safety: Safety incident counts are recorded for the period; derived rates are not shown due to data-quality concerns.

Bottlenecks: Open bottlenecks: 3; overdue: 0; critical: 0.

CRITICAL DECISIONS REQUIRED

1. aa
2. sgetdv
3. testing merge
4. sadf
5. sa

Overall Status	At Risk
Progress Status	Delay
Time Progress	99.00%
Cost Status	No Data
Open Bottlenecks	3
EOT Count	12
CPI	Not Available
SPI	Not Available

REPORT DATA NOTES

- Monthly progress data is not available for July 2026.
- Safety source data appears inconsistent; derived rates are not shown.
- Manpower data is not available for 2026-07.
- Meetings data is not available for 2026-07.
- Next Month Programme data is not available for 2026-07.
- Material Received data is not available for 2026-07.
- Laboratory Equipment data is not available for 2026-07.
- HSE rates unavailable: inconsistent manpower/working-days vs manhours.

2. SALIENT FEATURES OF THE PROJECT

A) Project	Satis Thane
C) Consultant	Shrikhande Consultants Limited
Project Start Date	09/08/2019
Original Contract Completion Date	08/12/2022
Current Completion Date	31/08/2026
Contract Value	Rs. 39,306,007.00
Revised Contract Value	Rs. 54,925,279.00
Project Duration (elapsed days)	2559
Approved EOT Count	11
Latest Approved EOT	EOT-13 (1362 days) — RLDA Changes
Team Leader	pmc_tl12

3. CONTRACTUAL OBLIGATIONS

Sr. No.	Particulars	Contract Provision	Details / Status	Validity
1	Performance BG of Rs.5,47,78,500/- Andhra Bank	As per contract	Status: Updated	17/10/2026
2	Performance BG of Rs. 2,55,63,300/-, IDBI Bank	As per contract	Status: Updated	20/08/2026
3	Retention Amount BG of Rs. 3,65,19,000/- Andhra Bank	As per contract	Status: Updated	26/06/2028
4	Retention Amount BG of Rs. 99,12,300/-	As per contract	Status: Updated	03/07/2028
5	Retention Amount BG of Rs. 57,38,700/-	As per contract	Status: Updated	17/11/2026
6	SCL BG (Migrated)	As per contract	Status: Updated	30/10/2027
7	Contract Value	Rs. 39,306,007.00	Revised: Rs. 54,925,279.00	—

EOT Status

EOT No.	Original Completion	Extension Days	Revised Completion	Reason	Status	Approval Date
13	08/12/2022	1362	31/08/2026	RLDA Changes	approved	23/07/2026
12	08/12/2022	151	31/05/2026	RLDA Changes	approved	12/03/2026
11	08/12/2022	275	31/12/2025	RLDA changes	approved	09/06/2025
10	08/12/2022	304	31/03/2025	RLDA Design changes	approved	17/08/2024
9	08/12/2022	428	31/05/2024	Railway GAD approval	approved	26/05/2023
8	06/03/2022	389	30/03/2023	Covid-19	approved	25/05/2022
7	08/12/2022	181	28/02/2027	RLDA design	pending	02/09/2026
6	08/12/2022	243	31/08/2026	RLDA- design changes	approved	12/03/2026
5	08/12/2022	275	31/12/2025	Railway Design Changes	approved	09/06/2025
4	08/12/2022	304	31/03/2025	Railway approval	approved	19/09/2024
3	08/12/2022	428	31/05/2024	GAD approval	approved	13/10/2023
2	08/12/2022	112	30/03/2023	Covid	approved	23/03/2023

Official completion (latest approved EOT): 31/08/2026

4. PROGRESS

4.1 Physical Progress

Monthly Progress

Monthly progress data is not available for July 2026.

Monthly Planned %	Not Available
Monthly Actual %	Not Available
Variance %	Not Available

Cumulative Progress

Cumulative Actual %	20.90%
Scope Planned Qty	177
Scope Completed Qty	37
Scope Progress %	20.90%

4.2 Bar Chart (Planned vs. Actual)

Physical Progress — July 2026

REPORTING PERIOD: JULY 2026

Historical Construction Progress

May 2026: Planned 45.00%, Actual 40.00%

Current reporting month (July 2026)

Monthly Construction Progress data is not available for July 2026.


Cumulative Scope KPI

Cumulative Scope Progress	20.90%
Scope Planned	177
Scope Completed	37

4.3 Financial Progress & Gross Monthly Work Done Value

Contract Value	Rs. 39,306,007.00
Revised Contract Value	Rs. 54,925,279.00
Monthly Work Done (ACWP)	—
Cumulative Work Done (BCWP)	—
Planned Value (BCWS)	—
Financial Progress %	0.00%
CPI	—
SPI	—
EAC	—
BAC	—
Cash In (Monthly Actual)	—
Cash Out (Monthly Actual)	—

Monthly Planned vs Actual Financial Progress

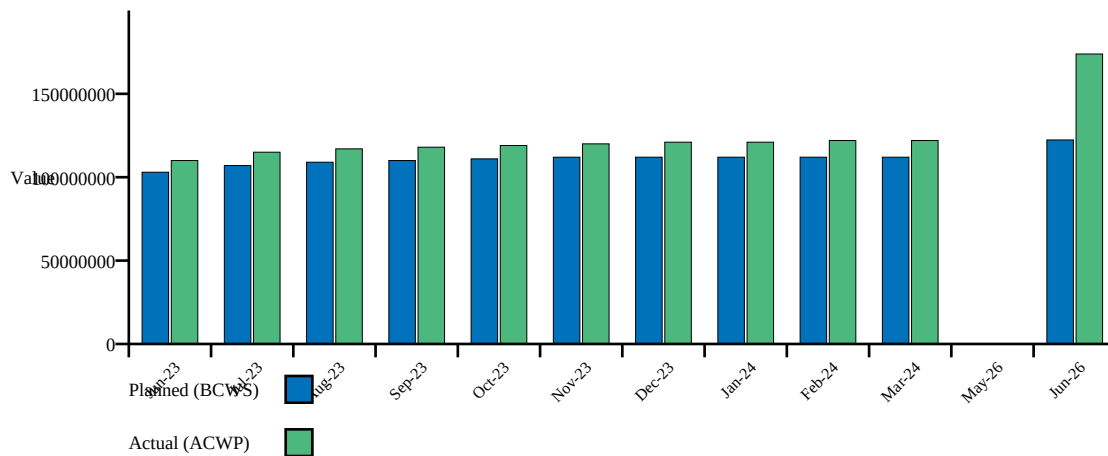

4.4 Important Events


Date	Event	Description	Status
25/05/2022	EOT-8	Covid-19	approved
23/03/2023	EOT-2	Covid	approved
26/05/2023	EOT-9	Railway GAD approval	approved
13/10/2023	EOT-3	GAD approval	approved
17/08/2024	EOT-10	RLDA Design changes	approved
19/09/2024	EOT-4	Railway approval	approved
09/06/2025	EOT-11	RLDA changes	approved
09/06/2025	EOT-5	Railway Design Changes	approved
12/03/2026	EOT-12	RLDA Changes	approved
12/03/2026	EOT-6	RLDA- design changes	approved
03/06/2026	Risk	www	Open
03/06/2026	Action	aa	Open
03/06/2026	Issue	budget	Open
02/07/2026	Client	testing scl	Delivered Late
02/07/2026	Client	sa	Pending
03/07/2026	Client	sadf	Pending
08/07/2026	Client	testing merge	Pending
08/07/2026	Contractor	testing	Delivered on Time
09/07/2026	Client	sgetdv	Pending
23/07/2026	EOT-13	RLDA Changes	approved
02/09/2026	EOT-7	RLDA design	pending

5. QUALITY PERFORMANCE

Tests Required	7050
Tests Conducted	7561
Tests Passed	7560
Tests Failed	1
Pass %	99.99%
Fail %	0.01%
Quality Performance	99.99
Shortfall	0

5.1 Material Testing / Frequency Chart

Material Testing Summary

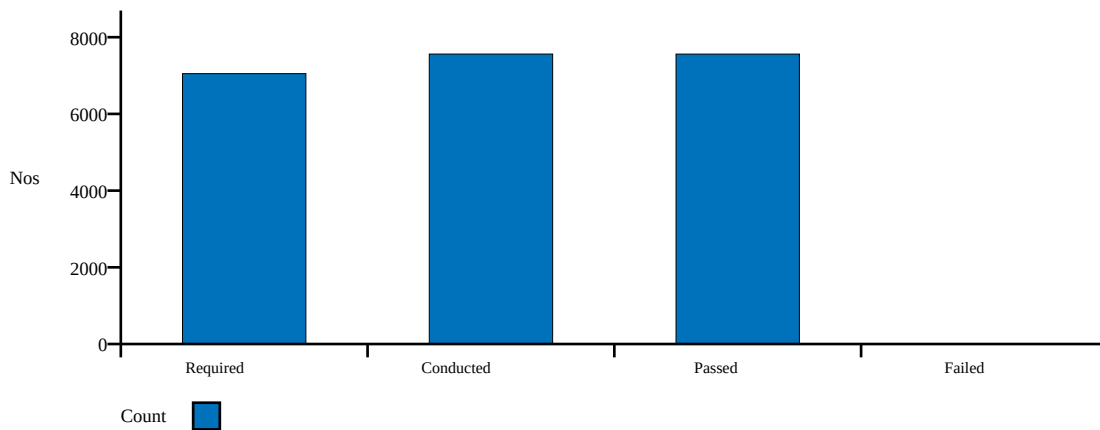

6. BOTTLENECKS

Sr. No.	Bottleneck	Category	Responsible Party	Date Raised	Target Resolution	Status	Days Open	Action Required
1	aa	ACTION	—	03/06/2026	—	Open	69	Monitor / resolve
2	www	RISK	—	03/06/2026	—	Open	69	Monitor / resolve
3	budget	ISSUE	—	03/06/2026	—	Open	69	Monitor / resolve

7. NEXT MONTH PROGRAM

Next month programme data is not available.

8. LIST OF PLANT AND MACHINERY

Total plant & machinery types: 26 | Total quantity: 2 | Source report date: 10/06/2026

Sr. No.	Equipment / Plant	Unit / Planned	Available / Actual	Deployment Status	Remarks
1	Equipment Deployment Summary	34	40	117.65%	—
2	Boom Lift	No	0	Not Available	—
3	C/B M/C	No	0	Not Available	—
4	DG set 20 & 62.5K VA	No	0	Not Available	—
5	De-watering pump	02	0	Not Available	—
6	Dumper	No	0	Not Available	—
7	Excavator	No	0	Not Available	—
8	Excavator breaker	No	0	Not Available	—
9	Hydra	Nos	0	Not Available	—
10	JCB	Nos	0	Not Available	—
11	Pickup	No	0	Not Available	—
12	Piling Rig Machine	Nos	0	Not Available	—
13	Piling Rig Tripod	Nos	0	Not Available	—
14	Piling rig tripod	No	0	Not Available	—

Sr. No.	Equipment / Plant	Unit / Planned	Available / Actual	Deployment Status	Remarks
15	Poclain	No	0	Not Available	—
16	Steel Cutting Machine	No	0	Not Available	—
17	Tower Crane	Nos	2	Working	—
18	Tractor Breaker	No	0	Not Available	—
19	Tractor De-watering pump	No	0	Not Available	—
20	Transit Mixer	Nos	0	Not Available	—
21	Water Tanker	Nos	0	Not Available	—
22	Welding M/C DG	No	0	Not Available	—
23	breaker m/c	01	0	Not Available	—
24	carens	2	0	Not Available	—
25	concrete vibrator 40 mm	02	0	Not Available	—
26	reinforcement bending m/c	01	0	Not Available	—
27	reinforcement cutting m/c	01	0	Not Available	—

9. LABORATORY EQUIPMENT AT SITE

Laboratory equipment register is not available.

10. STATUS OF DRAWINGS

STATEMENT SHOWING DESIGN & DRAWING STATUS

Sr. No.	Design / Drawing	Submission by Contractor	Reply by SCL	Status	Remarks
1	Dec (Rev 1)	19/12/2025	30/12/2025	Under Review	A
2	Jan (Rev 1)	10/01/2025	—	Under Review	B
4	Expansion Joint At Deck Level (Rev 3)	13/04/2026 08/06/2026	24/04/2026 23/06/2026	Approved	in Progress Approved on 23/06/2026
5	testing (Rev 22)	22/06/2026 22/06/2026	23/06/2026 25/06/2026	Approved	Approved Approved on 25/06/2026
6	test (Rev 1)	18/06/2026 22/06/2026	20/06/2026 26/06/2026	Under Review	in progress
7	testing (Rev 1)	09/07/2026 13/07/2026	11/07/2026 16/07/2026	Approved	approved Approved on 16/07/2026

10.1 Drawings Received

Total Drawings	6
Received	3
Reviewed	3
Approved	3
Pending	3

10.2 Drawings Balance

Pending Drawings	3
Pending with Contractor	3
Pending with PMC/SCL	0

11. MATERIAL RECEIVED AT SITE

Material received register is not available in the backend.

12. SAFETY ASPECT

Total Manhours	230
Man-Days Worked	0
Average Daily Manpower	0
Working Days	0
Total Incidents	651
Near Miss	87
Major Incidents	12
Minor Incidents	453
Significant Incidents	34
Fatalities	65
Reportable Accident (LTI)	0
LTIFR	Not Available
Incident Rate	Not Available
Loss of Manhours	123

13. MEETINGS / SITE VISITS

Meeting / site visit data is not available for the reporting period.

14. MANPOWER DEPLOYED (PMC)

PMC manpower data is not available for the reporting period.

15. LABOUR MAN-DAY BAR CHART

Labour man-day chart data is not available.

16. PHOTOGRAPHS



Site Photograph
03/07/2026



Site Photograph
03/07/2026



Site Photograph
03/07/2026



Site Photograph
03/07/2026
